BRUHAT BANGALORE MAHANAGARA PALIKE

Name of Work: Providing Walking track and other development works to Attur lake in Ward No.03 Attur

Sl No	Description of Work	Unit	Shedule-B Qty	Executed Qty	% of Work Completed
1	KSRRB 200-8. Clearing and grubbing road land including uprooting rank vegetation, grass, brush, shrubs, saplings and trees of girth upto 300mm, by manual means, in area of light jungle, removal of stumps, disposal of unserviceable materials, stacking of serviceable materials labour charges complete as per specifications. –do– thorney jungle	Sqm	1600.00	1596.76	99.80
2	KSRRB 300-1. Earthwork excavation by manual means for roads, drains & similar works in ordinary soil excavated surface levelled and sides neatly dressed, the disposed earth to be levelled neatly after breaking of clods complete as per specifications.	Cum	75.65	74.63	98.65
3	Removing and resetting of kerb stones	mtr	2656.00	2575.20	96.96
4	KSRB 4-1.6 ; Providing and laying in position plain cement concrete of Mix 1:2:4 with OPC @ 240kgs, with 20mm and down size graded granite metal coarse aggregates @ 0.878 cum and fine aggregtes @ 0.53cum, machine mixed, concrete laid in layers not exceeding 15 cms. thick, well compacted, in foundation, plinth and cills, including cost of all materials, labour, HOM curing complete as per	Cum	66.40	66.37	99.95
5	KSRRB 300-58. Compaction of original ground by mechanical means including filling in depression occuring during rolling including cost of all labour, HOM complete as per specifications.	Sqm	8170.00	8169.86	100.00
6	KSRRB M300-53. Construction of embankment with approved material Gravel/Murrum with all lifts and leads, transporting to site, spreading, grading to required slope and compacting to meet requirement Table 300-2 complete as per specifications, including cost of gravel / murrum, watering charges & compaction by vibratory roller to 95% of modified proctors density. MORTH	Cum	416.10	415.39	99.83
7	KSRB 4-1.2 : Providing and laying in position plain cement concrete of Mix 1:3:6 with OPC @ 220kgs, with 40mm and down size graded granite metal coarse aggregates @0.892cum and fine aggregates @ 0.465cum machine mixed, machine mixed, concrete laid in layers not exceeding 15 cms. thick, well compacted, in foundation including cost of all materials, labour, HOM curing complete as per specifications. Specification No. KBS 4.1, 4.2	Cum	1225.50	1225.48	100.00
8	KSRB 14.6 : Providing and laying heavy duty cobble stones interlock pavers, using cement and course sand for manufacture of blocks of approved size, shape and colour with a minimum compressive strength of 281 kg per sqm over 50mm thick sand bed (average thickness) and compacting with plate vibrator having 3 tons compaction force thereby forcing part of sand underneath to come up in between joints, final compaction of paver surface joints into its final	Sqm	8170.00	8169.86	100.00
9	Providing and fixing pre cast solid cement concrete kerb stones made out of C.C. 1:2:4 with top and bottom width 114 and 165 mm respectively, 400mm high and 450mm in length finished with CM 1:3 plastering and finishing cutting, including form work, curing, including cost of all materials, labour, hire charges of machinery, loading, unloading, lead and lift, transportation etc., complete.	Nos	1476.00	1473.00	99.80
10	KSRRB 800-1. Painting two coats after filling the surface with synthetic enamel paint in approved shades on new plastered concrete surfaces, with materials, labour complete as per specifications.	Sqm	1162.00	1133.37	97.54

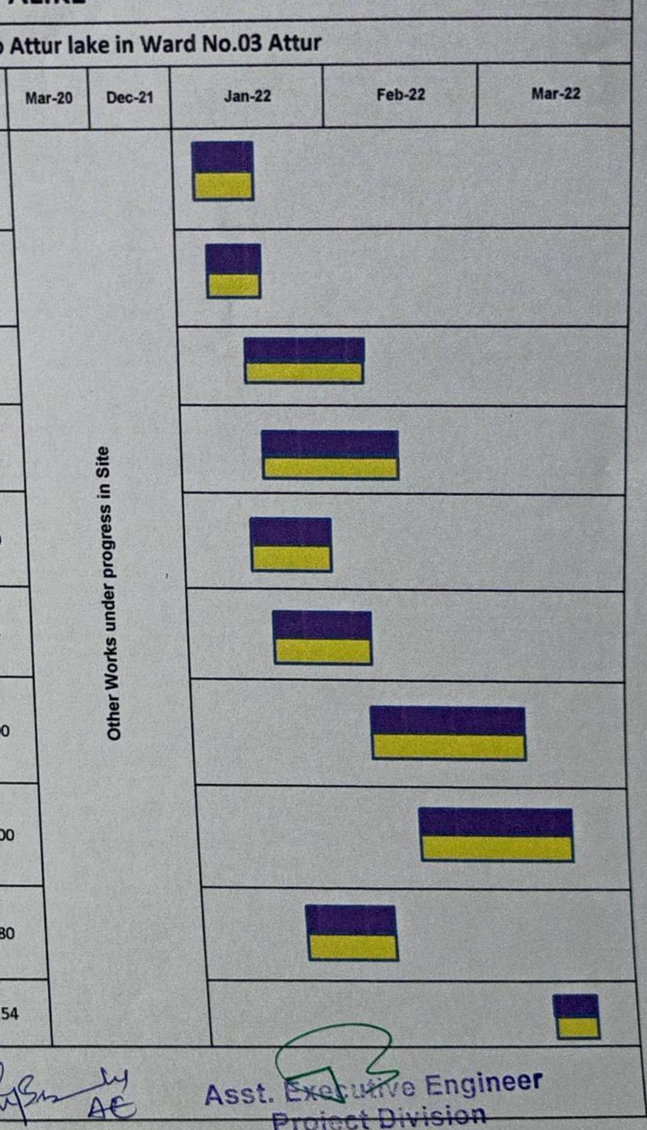

= Planned %
= Executed %

AE

Asst. Executive Engineer
Project Division
Yelahanka Zone

Scanned by TapScanner
